


Act ID	Description	Orig Dur	Early Start	Early Finish	2011												2012											
					JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL					
Permitting																												
1190	Notice to Proceed	7d	03JAN11	11JAN11	■ Notice to Proceed																							
1180	Site specific Plan Fencing	4d	12JAN11	17JAN11	■ Site specific Plan Fencing																							
1210	Utility Permit	5d	12JAN11	18JAN11	■ Utility Permit																							
1200	Swipp Plan	5d	18JAN11	24JAN11	■ Swipp Plan																							
1250	Building Permit	8d	20JAN11	31JAN11	■ Building Permit																							
Sitework																												
1260	Site Demolition Partial demo of Bldg @	5d	28FEB11 A	04MAR11	■ Site Demolition Partial demo of Bldg @ new FDTN																							
1280	Salvage noted site materials	2d	03MAR11	04MAR11	■ Salvage noted site materials																							
1010	Erosion Control Measures Bld Const	8d	07MAR11	25MAR11	■ Erosion Control Measures Bld Const Entrance																							
1270	Clear and Grub	10d	07MAR11	18MAR11	■ Clear and Grub																							
1310	Excavate and backfill foundations	42d	09MAR11	29APR11	■ Excavate and backfill foundations																							
1290	Storm Drainage/Sewer	12d	02MAY11	20MAY11	■ Storm Drainage/Sewer																							
1300	Domestic Water service	6d	20MAY11	27MAY11	■ Domestic Water service																							
1370	Fine Grade site	10d	30MAY11	06JUN11 A	■ Fine Grade site																							
1360	Binder Parking areas	5d	24JUN11 A	28JUN11 A	■ Binder Parking areas																							
1350	Gravel SOG	12d	11AUG11	26AUG11	■ Gravel SOG																							
1340	Underslab utilities	20d	16AUG11 *	13SEP11	■ Underslab utilities																							
1380	Gravel Sidewalks	6d	16MAY12	23MAY12	■ Gravel S																							
1390	Install Curbing	4d	16MAY12	21MAY12	■ Install C																							
1400	Finish pave	3d	24MAY12	28MAY12	■ Finish p																							
1410	Hardscape	5d	28MAY12	01JUN12 A	■ Hardsc																							
1420	Landscape	6d	04JUN12 A	11JUN12 A	■ Land																							
Concrete																												
1460	Footings and Walls	35d	09MAR11	29APR11	■ Footings and Walls																							
1480	Isolation footings	20d	17MAR11	27APR11	■ Isolation footings																							
1490	Slab on Decks	10d	04JUL11 A	15JUL11 A	■ Slab on Decks																							
1440	Slab on Grade	5d	29AUG11	02SEP11	■ Slab on Grade																							
1450	Concrete Walks	5d	18MAY12	24MAY12	■ Concrete																							
Masonry																												
1030	Exterior CMU + Brick Veneer	54d	26JUL11 A	07OCT11	■ Exterior CMU + Brick Veneer																							
1500	CMU Gymnasium Elevator Shaft	15d	26SEP11 A	14OCT11	■ CMU Gymnasium Elevator Shaft																							
Structural Steel/Mic Metals																												
1040	Derick 1 Area - A	25d	12MAY11	15JUN11 A	■ Derick 1 Area - A																							
1510	Derick 2 Area - B	8d	08JUN11 A	17JUN11 A	■ Derick 2 Area - B																							
1520	Derick 3 Area -C	5d	15JUN11 A	21JUN11 A	■ Derick 3 Area -C																							
1530	Misc Metals	40d	15AUG11	20JUN11 A	■ Misc Metals																							
Carpentry																												

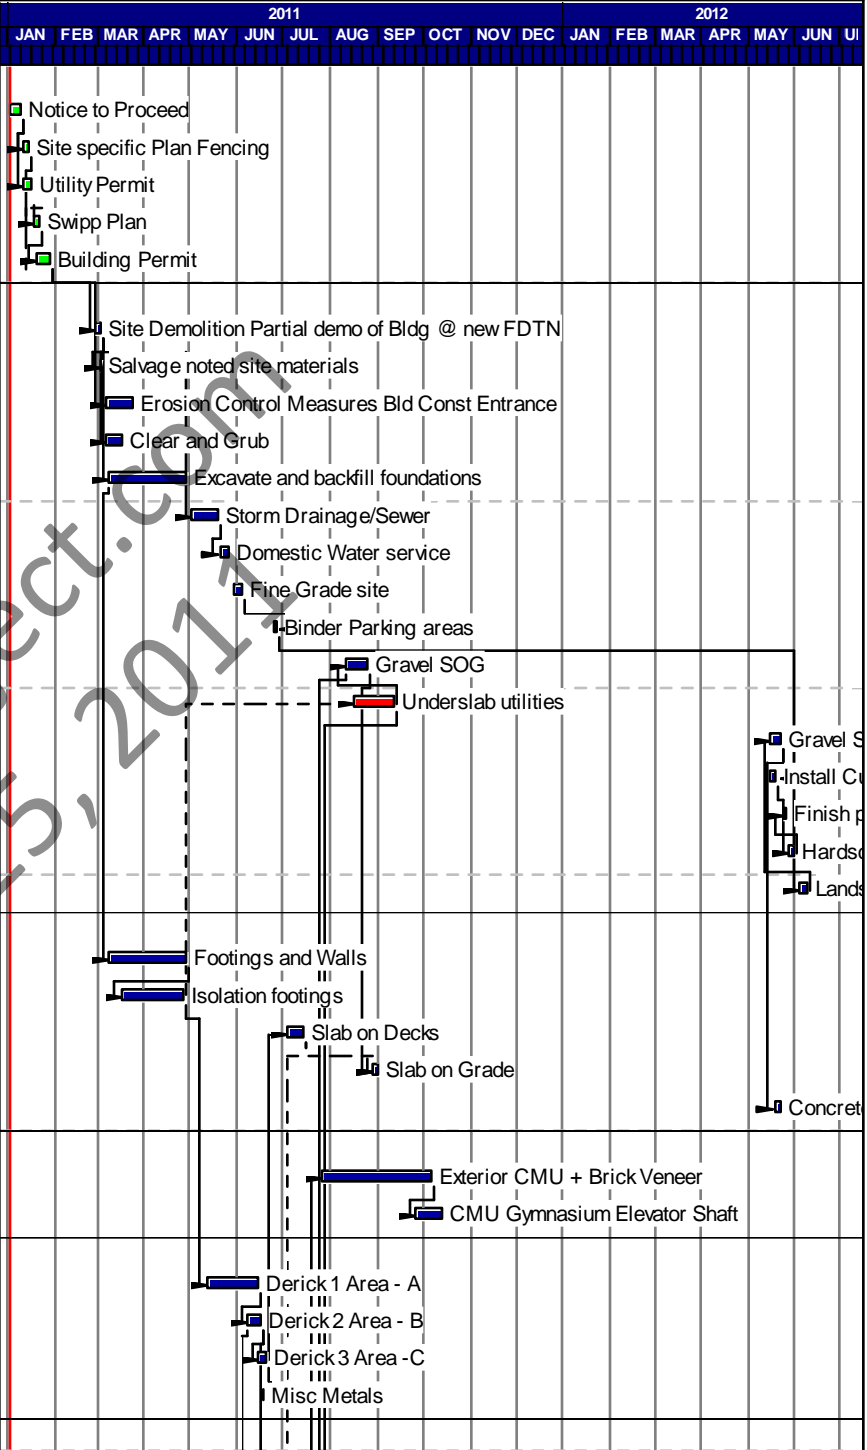

Start date	03JAN11
Finish date	15JUN12
Data date	03JAN11
Run date	25JAN11
Page number	1A
© Primavera Systems, Inc.	

Conant Elementary School Harvey Construction

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

