

Act ID	Description	Orig Dur	Early Start	Early Finish
Permitting				
1180	Site specific Plan	3d	19JAN11 A	21JAN11 A
1190	Notice to Proceed	5d	19JAN11 A	25JAN11 A
1200	Swipp Plan	5d	21JAN11 A	27JAN11 A
1210	Utility Permit	5d	24JAN11 A	28JAN11 A
1250	Building Permit	1d	31JAN11 A	31JAN11 A

Asbestos Abatement+Bldg demolition				
1240	Salvage Owner Materials	1d	07JAN11 A	07JAN11 A
1170	State Approval for Abatement	10d	12JAN11 A	25JAN11 A
1230	Abate Buildings	20d	27JAN11 A	28FEB11 A
1220	Demolish Buildings	35d	07FEB11 A	25MAR11


Sitework				
1010	Erosion Control Measures	8d	07MAR11	16MAR11
1310	Excavate and backfill foundations	45d	14MAR11	13MAY11
1260	Site Demolition	12d	31MAR11	15APR11
1270	Clear and Grub	10d	14APR11 A	27APR11
1280	Salvage noted site materials	8d	18APR11 A	27APR11
1290	Storm Drainage/Sewer	12d	18APR11 A	03MAY11
1300	Domestic Water service	6d	09MAY11	16MAY11
1340	Under slab utilities	20d	16MAY11	10JUN11
1350	Underdrain and Gravel SOG	15d	23MAY11	10JUN11
1370	Fine Grade site	20d	27MAY11	23JUN11
1360	Binder Parking areas	5d	17JUN11 A	23JUN11
1380	Gravel Sidewalks	6d	25MAY12	01JUN12
1420	Landscape	6d	01JUN12 A	08JUN12
1390	Install Curbing	4d	04JUN12 A	07JUN12
1410	Hardscape	5d	11JUN12 A	15JUN12
1400	Finish pave	6d	15JUN12 A	22JUN12

Concrete				
1460	Footings and Walls+Shot Crete ret wall	30d	21MAR11	29APR11
1480	Isolation footings	20d	11APR11 A	06MAY11
1490	Slab on Decks	4d	30MAY11	02JUN11
1440	Slab on Grade	10d	13JUN11 A	24JUN11
1450	Concrete Walks	5d	04JUN12 A	08JUN12

Masonry				
1500	CMU GYM and Elevator Shaft	15d	02MAY11	20MAY11
1030	Brick Veneer East to West	60d	04JUL11 A	23SEP11 A

Structural Steel/Mc Metals				
1040	Derick 1 East	25d	25APR11 A	27MAY11
1510	Derick 2 West	8d	19MAY11	30MAY11
1520	Derick 3 West	5d	26MAY11	01JUN11
1530	Misc Metals	40d	04JUL11 A	26AUG11

Carpentry				
1050	Rough Carpentry	20d	27OCT11 A	23NOV11

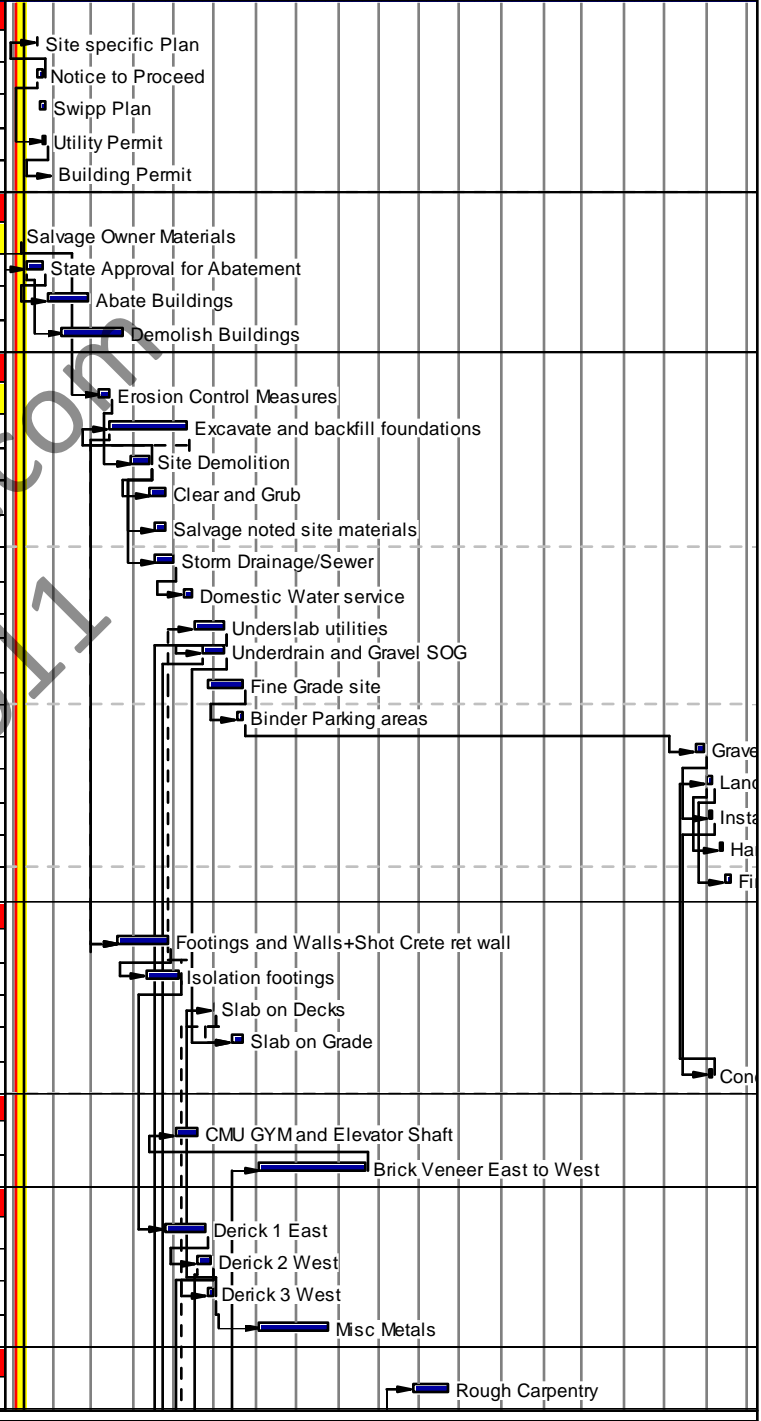

Start date 03JAN11
 Finish date 15JUN12
 Data date 03JAN11
 Run date 02FEB11
 Page number 1A
 © Primavera Systems, Inc.

Kimball Elementary School Harvey Construction

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

